



EUROPEAN CENTRAL BANK

EUROSYSTEM

T2-T2S Consolidation Status Update

TARGET Consolidation
Contact Group (TCCG)

9 December 2020

ECB-UNRESTRICTED
UPDATABLE



DG Market Infrastructure and Payments
T2-T2S Consolidation

Agenda

A Project Workstreams

B Change Management

C Consultations with Eurosystem Committees

A. Project Workstreams

1 Product Readiness

Specifications phase

Development phase


Testing and Migration

2 Community Readiness

3 Operational Readiness

4 Legal Readiness

High-level timeline

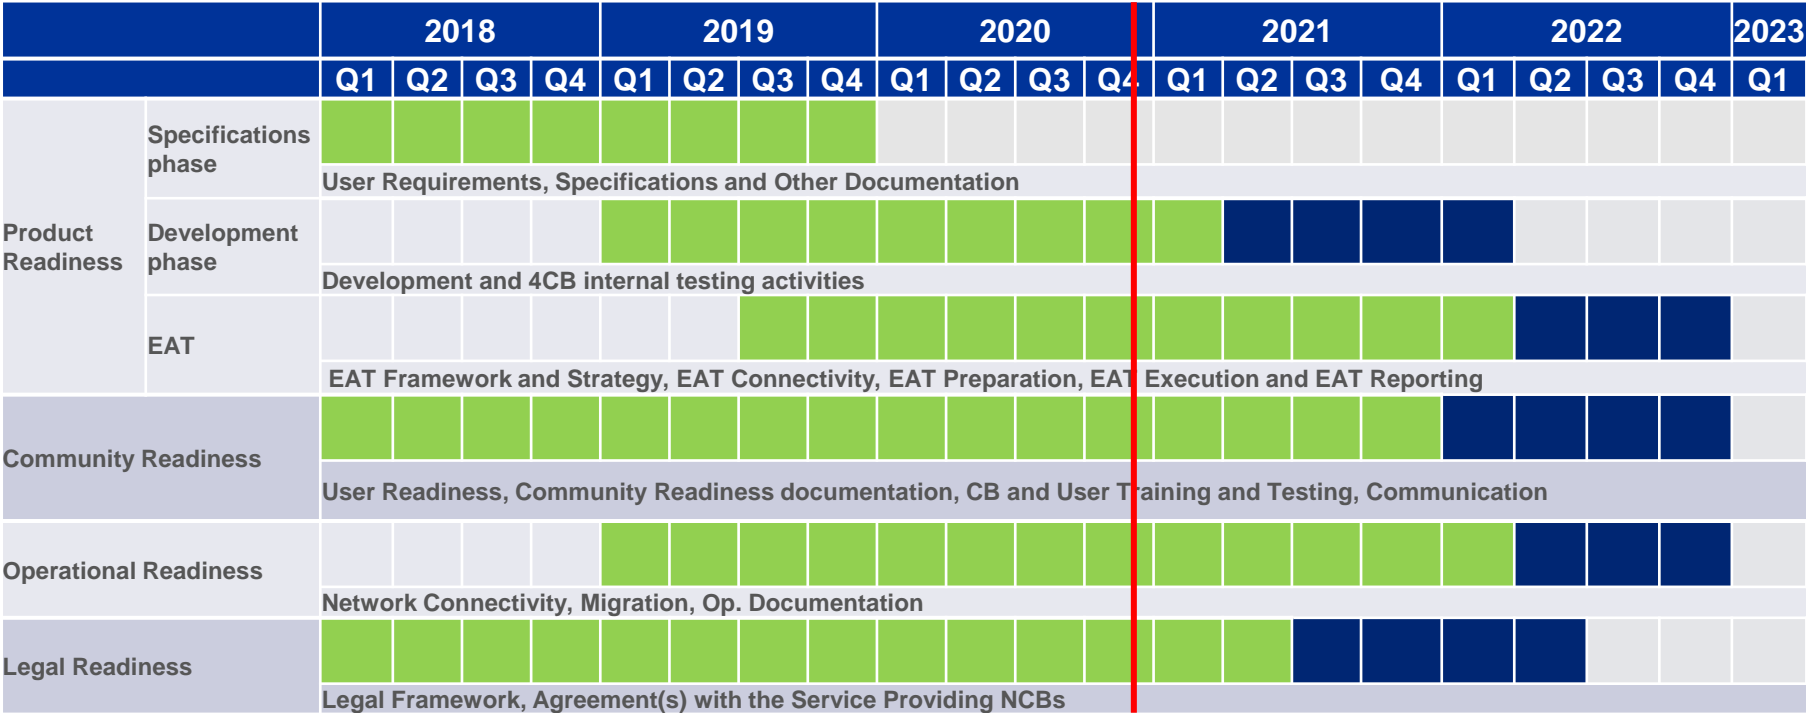

Specifications phase

UDFS

- **UDFS v2.2**
 - Some chapters to be further complemented (e.g. editorial changes, pending change requests)
 - To be published in Q1 2021 (to be validated)

Change Requests


- Critical CRs published on ECB website

UHB

- **UHB v1.0**
 - BILL UHB v1.0 published on ECB website on 30 November
 - RTGS and CLM UHB v1.0 to be published by the end of December 2020

Development phase

- Development is progressing according to plan



Testing and Migration

- ☑ Planned delivery dates for public versions of Testing and Migration deliverables stemming from re-planning are presented in the below table:

Deliverables	Planned delivery dates
User Testing calendar <u>v1.0</u>	01.02.2021
Connectivity Guide <u>v1.0</u>	01.02.2021
TARGET Services Registration and On-boarding guide (including form) <u>v1.0</u>	26.02.2021
User Testing Reporting Framework <u>v1.0</u>	01.03.2021
Migration Strategy (T2 Migration, Readiness and Testing Strategy) <u>v2.0</u>	05.03.2021
T2 User Testing Terms of Reference (UT ToR) <u>v1.0</u>	01.06.2021
T2 Mandatory test cases <u>v1.0</u>	30.06.2021

A. Project Workstreams

1 Product Readiness

Specifications phase

Development phase

Testing and Migration

2 Community Readiness

3 Operational Readiness

4 Legal Readiness

Community Readiness

- The list of T2-T2S Consolidation project key milestones for participants has been published last month on the ECB website under the following link:

https://www.ecb.europa.eu/paym/target/consolidation/profuse/shared/pdf/T2_T2S_Consolidation_Key_milestones_for%20participants_Short_Description.pdf

- The document for the Key milestones for participants (including Detailed Description) has been shared with the TCCG for a written procedure until Thursday 10 December 2023

A. Project Workstreams

1 Product Readiness

Specifications phase

Development phase

Testing and Migration

2 Community Readiness

3 Operational Readiness

4 Legal Readiness

Operational Readiness

- ❑ Drafting of the operational documentation is going
- ❑ A stable version of the Infoguide to be delivered in October 2021

Please note that some dates are subject to final approval

Thank you for your attention!



T2-T2S.Consolidation@ecb.europa.eu

www.ecb.europa.eu/paym



ECB: market infrastructure and payments
